
1.PERT Chart

PERT stands for Program Evaluation and Review Technique. It is used to identify project activities, their durations, and the dependencies between them.

Project Activities

Activity	Task Name	Duration	Depends On
A	System Request	2 days	—
B	Feasibility Study	3 days	A
C	Methodology and Time Estimation	2 days	B
D	Case Study	3 days	C
E	Interview Questions	3 days	D
F	Web Form Questionnaire	2 days	D
G	Interview Report	2 days	E, F
H	Data Flow Diagram	3 days	G
I	Process Specification	2 days	H
J	Data Modeling	3 days	I
K	Final Documentation and Review	2 days	J

Pert Chart (MS-Project)

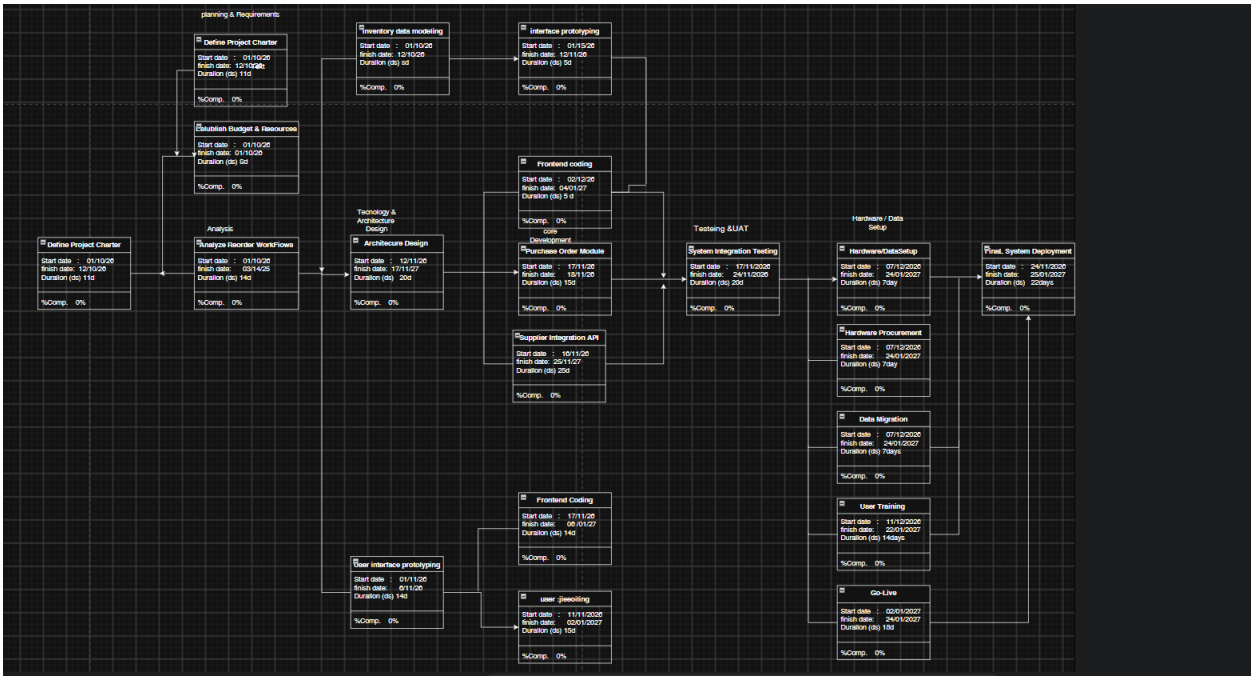

2. Gantt Chart

A Gantt chart shows project activities on a timeline, including their planned start dates, end dates, and durations.

Project Schedule

Activity	Task Name	Start Date	End Date	Duration
A	System Request	01/11/2026	02/11/2026	2 days
B	Feasibility Study	03/11/2026	05/11/2026	3 days
C	Methodology and Time Estimation	06/11/2026	07/11/2026	2 days
D	Case Study	08/11/2026	10/11/2026	3 days
E	Interview Questions	11/11/2026	13/11/2026	3 days
F	Web Form Questionnaire	11/11/2026	12/11/2026	2 days
G	Interview Report	14/11/2026	15/11/2026	2 days
H	Data Flow Diagram	16/11/2026	18/11/2026	3 days
I	Process Specification	19/11/2026	20/11/2026	2 days
J	Data Modeling	21/11/2026	23/11/2026	3 days
K	Final Documentation and Review	24/11/2026	25/11/2026	2 days

Gantt chart (MS-Project)

